



LETU Abbott Aviation Renovation & Addition

Construction Progress Report

06.10.26

Report Summary:

- Building pad
- OLL spread footings



Site as Pictured 06.10.2026

Progress Report:

Earthwork/Civil:

- Survey and structural fill on building pad
- Proof rolling complete and passed
- Select fill at hangar complete and passed
- Footer excavation for OLL reinforcement
- Concrete placement for spread footings at OLL
- Under slab plumbing






32.39275, -94.70510
Jun 5, 2026 at 2:19:28 PM CDT

Looking Ahead: Over the next 3-Weeks

- Under slab plumbing
- Power from transformer to fire pump room
- Excavate and pour elevator pit

Milestones & Metrics:

- Total Onsite Manhours to Date: 4,053
- Accumulated rainfall to date: 14.16"

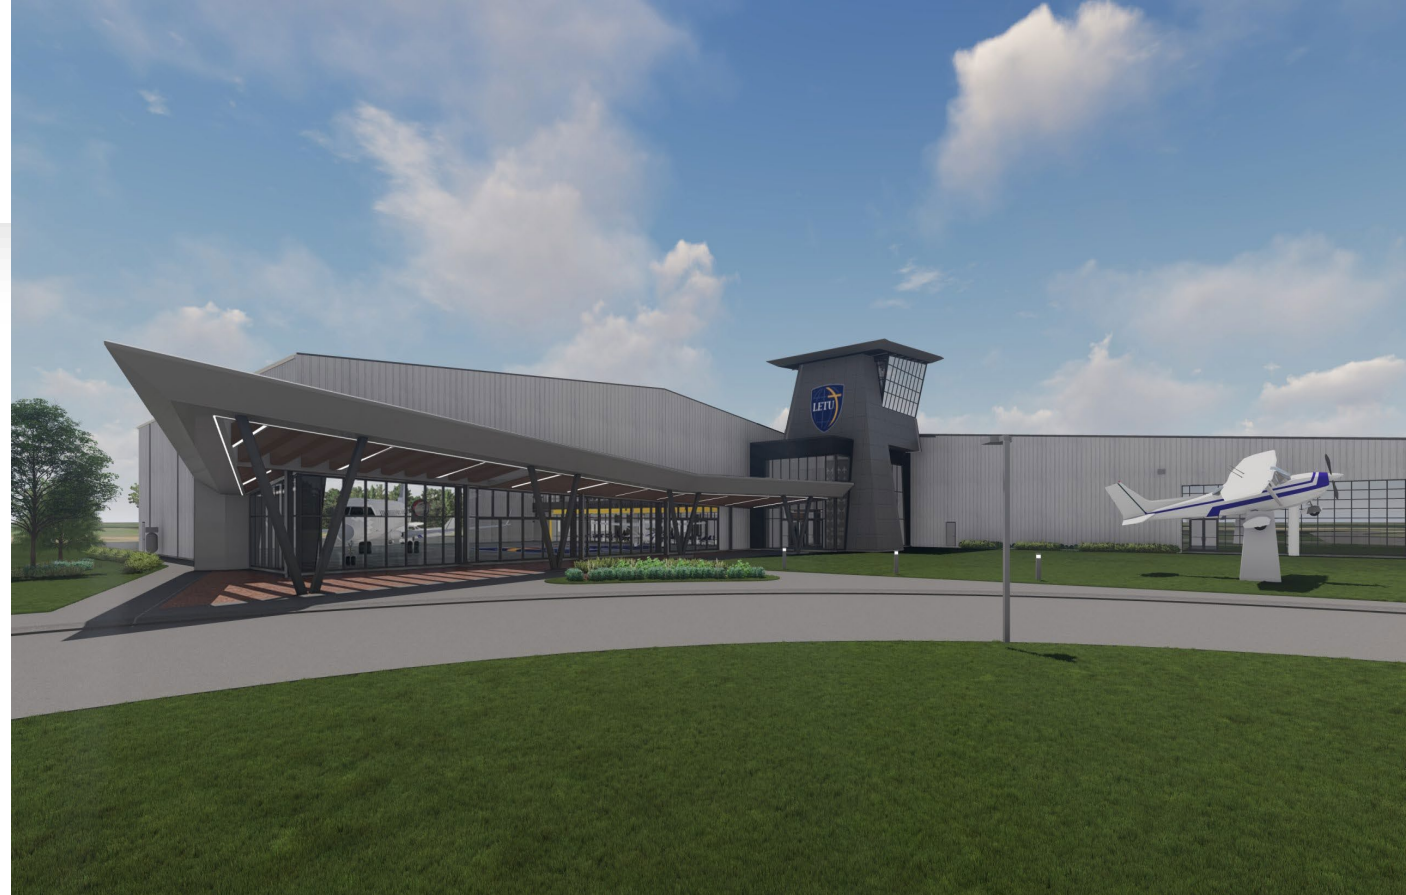

*“More detail is available on the Master Schedule & 3-week “Look-ahead.”
For additional information, please contact Brian Prescott with Transet Co.*
