



LETU Athletic & Human Performance Air Dome Project

Construction Progress Report

02.26.26

Report Summary:

- New Northwest Parking Lot has begun
- Courtyard in Progress
- Interior Painting Completed
- Exterior Roadwork in progress



Site as Pictured 02.25.2026


Progress Report:

Earthwork/Civil:

- Courtyard Planter Walls in progress.
- Courtyard lighting installations & power-up nearly completed.
- Exterior flatwork in progress.
- PRs 15, 30, and 33 earthwork in progress. Includes underground utilities relocation.
- Additional 300 KVA Transformer energized.

Lobby Building:

- Finish work in progress.
- Access Controls work in progress.
- Lighting controls completed.
- Data racks nearing completion.
- Fire Alarm, detection, and notification devices nearly completed.

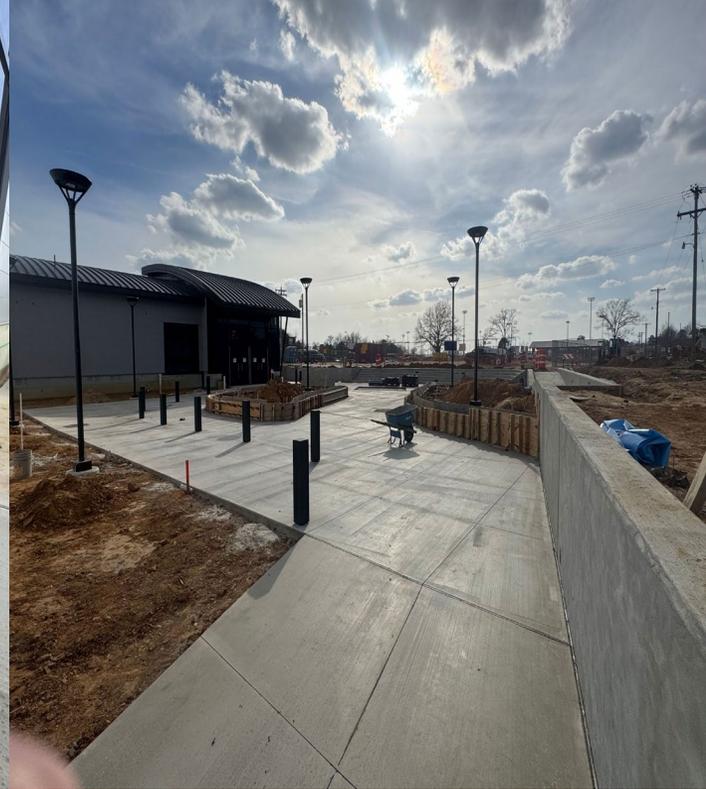

Progress Report:

Athletic & Human Performance Buildings (Units B & C):

- Putting Green, framing, electrical, data for PRs 29R2 and 32 in progress.
- Data cabling installation is in progress.
- Data racks nearing completion.
- Access Controls work in progress.
- Track floor installation in progress.
- Fire Alarm, detection, and notification devices nearly completed.
- Wheelchair lift completed.

Fire Pump House

- Pumps and controls installation in progress.





Milestones & Metrics:

Manhours this reporting period:	3688
Total Onsite Manhours to Date:	96,457
Volume of Select Fill installed to Date:	37,369 CY
Volume of Concrete Placed to Date:	6,195 CY
Rain Events since last report:	2
Rainfall to Date in February:	1.94"
Total Rainfall Year-to date:	4.40"



Looking Ahead: Over the next 3-Weeks

Earthwork/Civil:

- North parking lots and roads including PRs 15, 30, and 33 changes.
- Flat work at dome building perimeter.
- Courtyard flatwork, planters, logo pavers.
- Paving Fire Apparatus Access Road.
- Retaining wall guardrails.
- Remainer of site lighting – pole lights.

Athletic & Human Performance Buildings:

- Fiber Optic / Network service.
- A/V devices installation.

Lobby Building & Pump House:

- Fiber Optic / Network service.
- Gutters, downspouts installation.
- Restrooms completion.
- Fire Pump Testing & Commissioning.
- Water Cannon testing.

Dome & Track

- Track floor installation.
- Scoreboard & timing systems data / comm.
- Finalize fire detection/notification and suppression systems.



*“More detail is available on the Master Schedule & 3-week “Look-ahead.”
For additional information, please contact Garry Phillips with Transet Co.*
