



LETU Abbott Aviation Renovation & Addition

Construction Progress Report

04.29.26

Report Summary:

- Flushing and testing water
- Fire Riser Work
- Underground utility removal



Site as Pictured 04.29.2026

Progress Report:

Earthwork/Civil:

- Flushing Water main for testing
- Rain recorded 4/27/26
- Anchor bolts delivered






Looking Ahead: Over the next 3-Weeks

- Complete COL testing requirements for 8” water line.
- Route new line to existing fire riser
- Remove existing Water and Sewer lines
- Excavation of subgrade for foundation.

Milestones & Metrics:

- Total Onsite Manhours to Date: 2,478
- Accumulated rainfall to Date: 7.45”

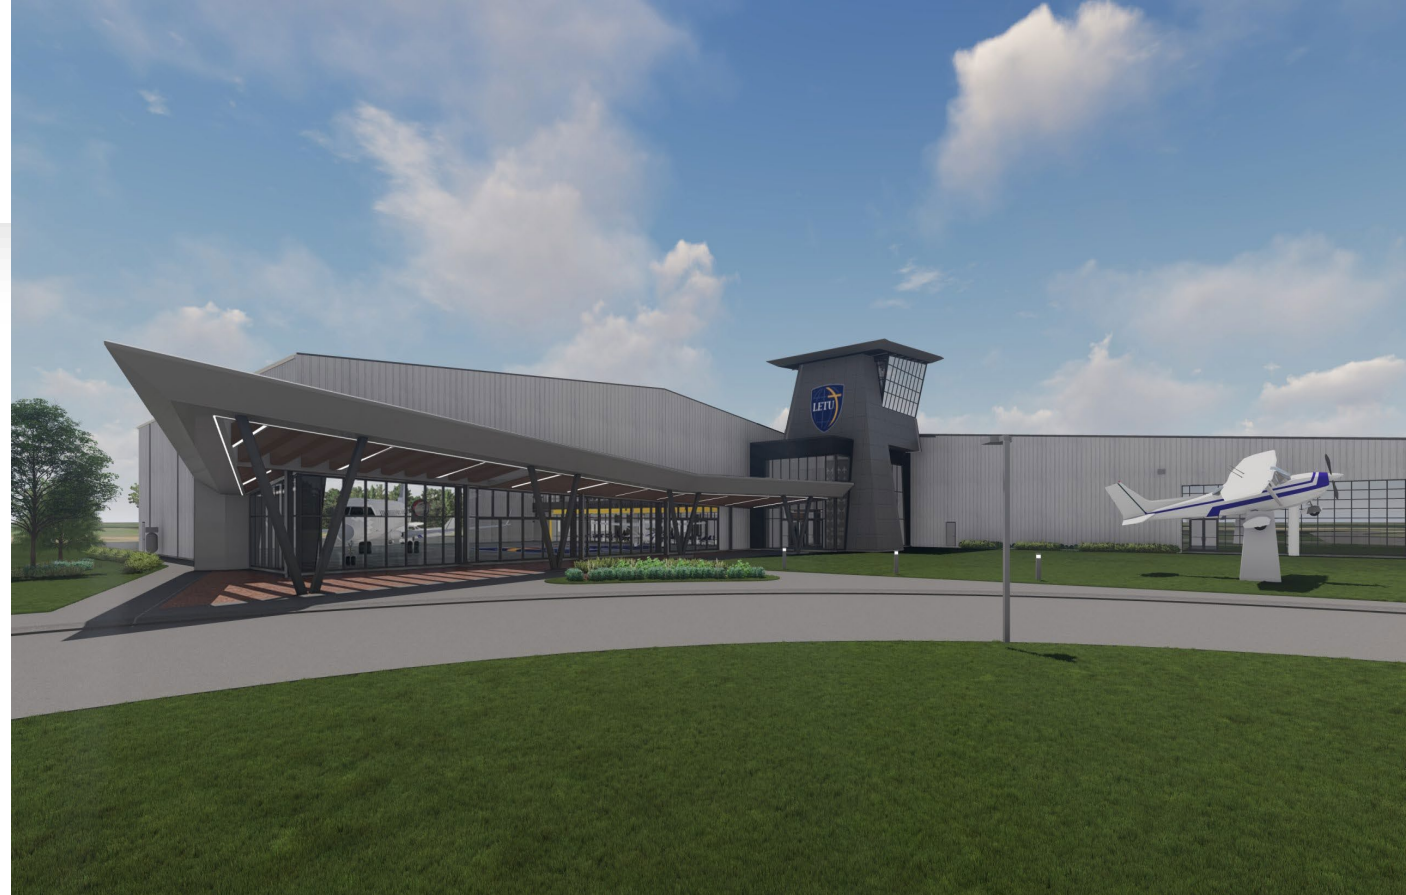

*“More detail is available on the Master Schedule & 3-week “Look-ahead.”
For additional information, please contact Brian Prescott with Transet Co.*
