



LETU Athletic & Human Performance Air Dome Project

Construction Progress Report

04.09.26

Report Summary:

- Track surface installation continues
- Society Drive Expansion underway
- Exterior Landscaping & Irrigation have begun



Progress Report:

Earthwork/Civil:

- Northwest parking lot nearing completion.
- Weller / Society Drives demolition completed.
- Weller / Society Drives grading, curb/gutter in progress.
- Additional natural gas line relocations in progress.
- East retaining wall guardrails installed, ready for paint.
- Landscaping / irrigation sprinklers in progress..

Lobby Building:

- OFCI appliances installation nearing completion.
- Preliminary punch list work in progress.
- I/T Room 110 network buildout in progress (LETU Staff).




Progress Report:

Athletic & Human Performance Buildings (Units B & C):

- Track floor installation in progress.

Fire Pump House

- Preliminary punch list work in progress.
- Water cannons flow tested & inspected by City.

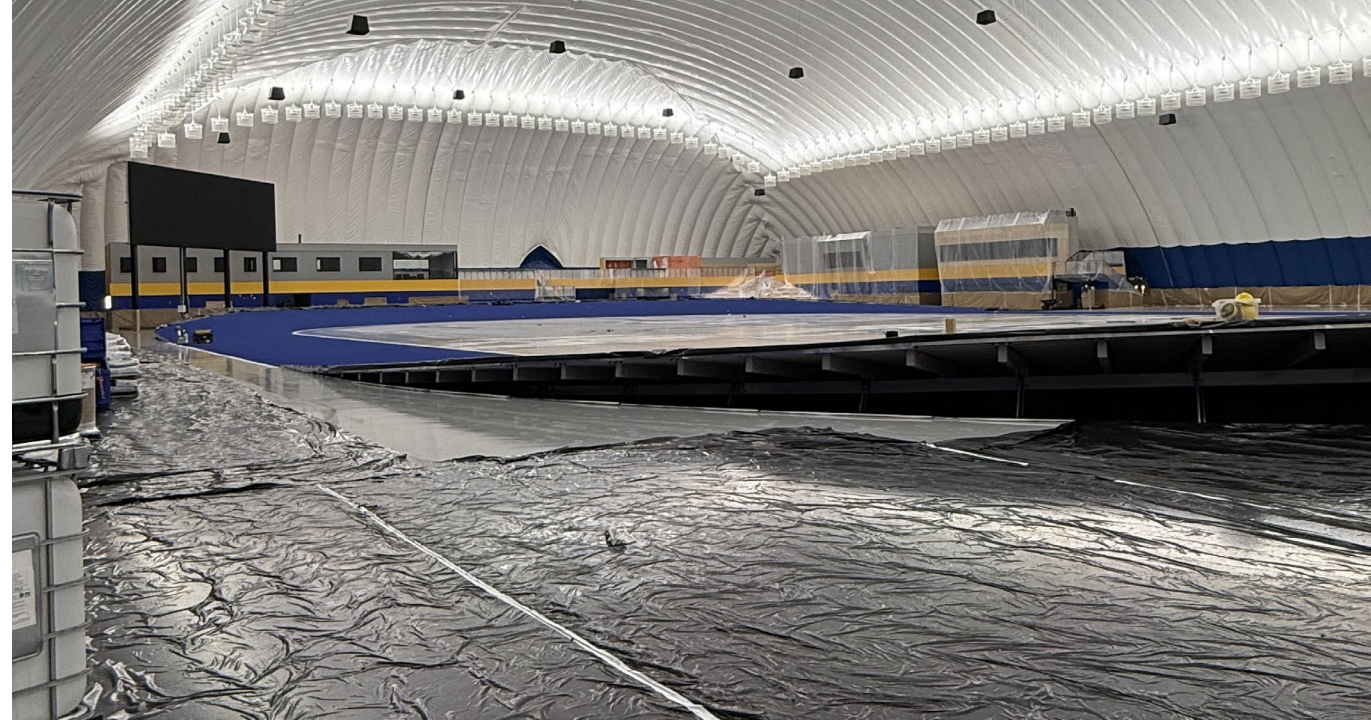



Milestones & Metrics:

Manhours this reporting period:	2,648
Total Onsite Manhours to Date:	103,657
Volume of Select Fill installed to Date:	37,369 CY
Volume of Concrete Placed to Date:	6,381 CY
Volume of TXDOT Type A, Grade 1 road base installed since last report: ~ 750 tons	
Rain Events since last report:	2
Rainfall to Date in April:	2.43"
Total Rainfall Year-to date:	9.38"



Looking Ahead: Over the next 3-Weeks

Earthwork/Civil:

- Sidewalks
- West retaining wall and courtyard guardrails/handrails.
- Remainder of site lighting – pole lights.
- Courtyard changes.

Athletic & Human Performance Buildings:

- All remaining work scheduled to resume ~ 4/25/26 pending track floor completion.

Lobby Building & Pump House:

- Fiber Optic / Network service finalization.
- A/V devices installation.
- Remainder of masonry work.
- Carpet installation.

Dome & Track

- Track floor completion including striping.
- Athletic equipment installation.

Pump House

- Fire Alarms final programming, testing, inspection



*“More detail is available on the Master Schedule & 3-week “Look-ahead.”
For additional information, please contact John Flahie with Transet Co.*
