



# LETU Athletic & Human Performance Air Dome Project

Construction Progress Report

04.23.26

# Report Summary:

- Track surface almost complete
- Society Drive Expansion underway
- Exterior Landscaping & Irrigation have begun



Site as Pictured 04.22.2026

# Progress Report:

## Earthwork/Civil:

- Northwest parking lot ready for paving.
- Weller / Society Drives soil stabilized, ready for road base & curb and gutter.
- Landscaping / irrigation sprinklers in progress.
- Sidewalks north of dome in progress.

## Lobby Building:

- Courtyard light bollards removed, concrete replaced.
- Masonry installation at Lobby Building nearing completion.
- Prep for masonry at courtyard planters in progress.



# Progress Report:


## Athletic & Human Performance Buildings (Units B & C):

- Track floor installation scheduled to finalize this week.

## Fire Pump House

- U/G fire water lines and appurtenances inspected by City.



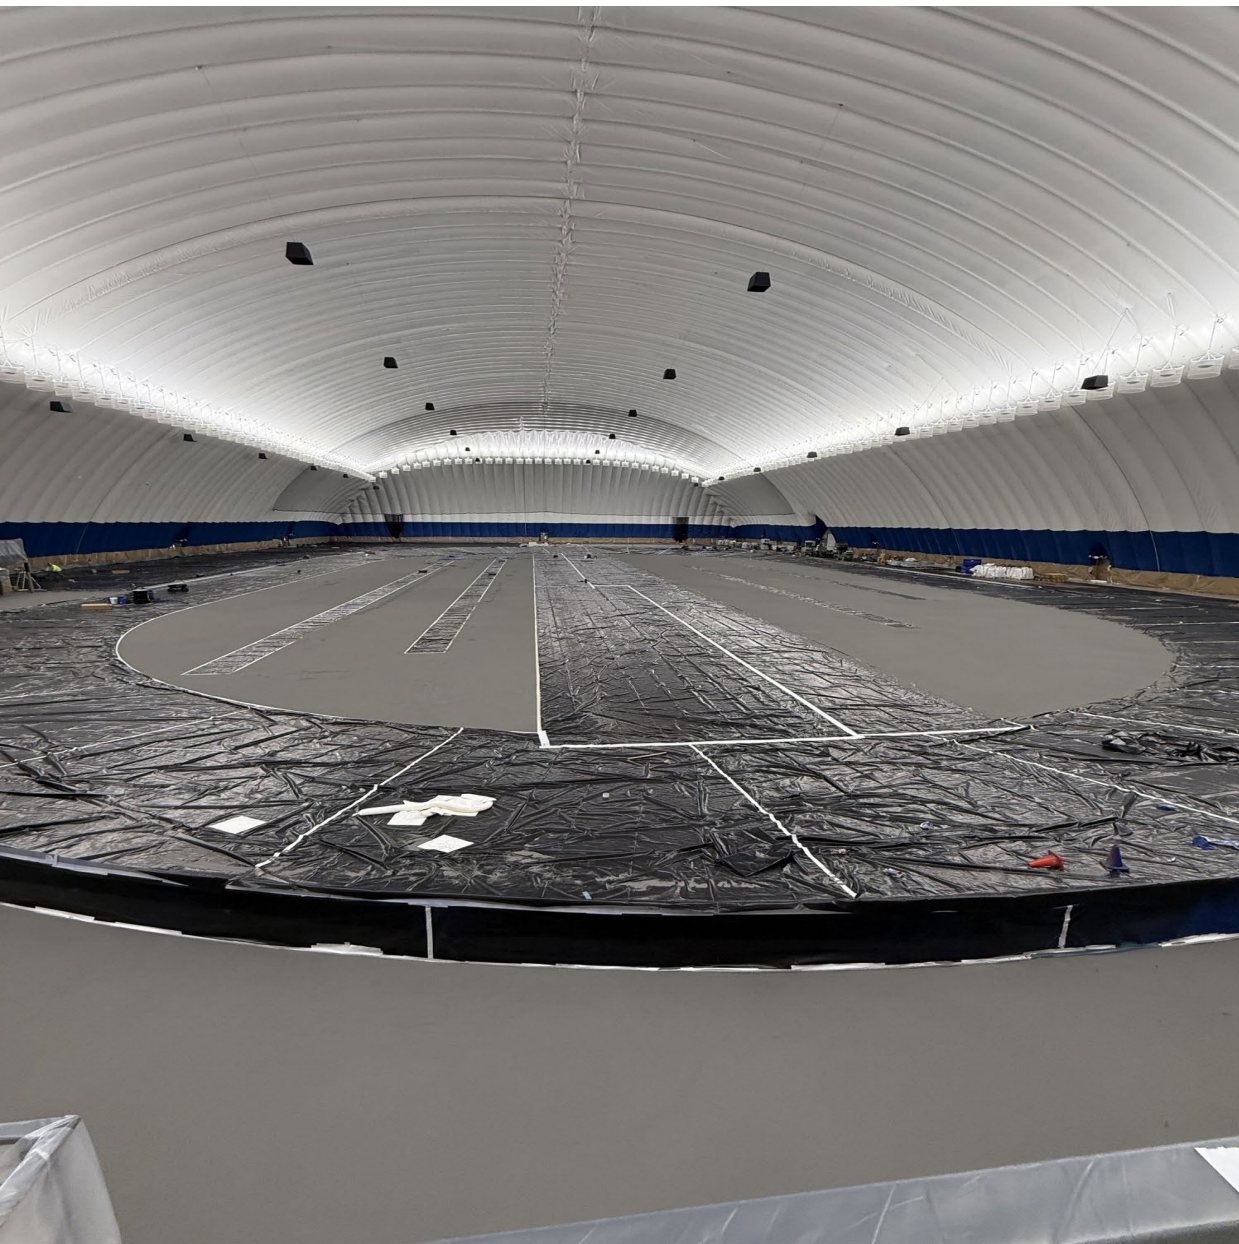

# Milestones & Metrics:

Manhours this reporting period:	2,696
Total Onsite Manhours to Date:	106,353
Volume of Select Fill installed to Date:	37,369 CY
Volume of Concrete Placed to Date:	6,426 CY
Volume of TXDOT Type A, Grade 1 road base installed since last report: ~ 900 tons	
Rain Events since last report:	3
Rainfall to Date in April:	3.06"
Total Rainfall Year-to date:	10.01"



# Looking Ahead: Over the next 3-Weeks

## Earthwork/Civil:

- Sidewalks
- West retaining wall and courtyard guardrails/handrails.
- Remainder of site lighting – pole lights.
- Weller & Society Drive road base, curb/gutter, paving

## Athletic & Human Performance Buildings:

- All remaining work scheduled to resume ~ 4/27/26 pending track floor completion.

## Lobby Building & Pump House:

- Fiber Optic / Network service finalization.
- A/V devices installation.
- Carpet installation.

## Dome & Track

- Track floor striping.
- Athletic equipment installation.

## Pump House

- Fire Alarms final programming, testing, inspection



*“More detail is available on the Master Schedule & 3-week “Look-ahead.”  
For additional information, please contact John Flahie with Transet Co.*
